



ID	Task Name	Duration	Start	Finish	Predecessors	October							November					
						23/09	30/09	07/10	14/10	21/10	28/10	04/11	11/11	18/11	25/11	02/12		
1	Apoint SPM (on sample scheme)	0 days	Fri 25/10/13	Fri 25/10/13														
2	Initial Engagement and Design Proposals	8 wks	Fri 09/01/15	Thu 05/03/15														
3	Future Schools Proposal (FSP) submitted	1 day	Fri 06/03/15	Fri 06/03/15	2													
4	Future Schools Proposal Evaluation	2 wks	Mon 09/03/15	Fri 20/03/15	3													
5	Prepare planning application/ Consultation	4 wks	Mon 23/03/15	Fri 17/04/15	4													
6	Planning Submission	0 days	Fri 17/04/15	Fri 17/04/15	5													
7	Planning determination period	13 wks	Mon 20/04/15	Fri 17/07/15	6													
8	Receive formal Planning Approval	0 days	Fri 17/07/15	Fri 17/07/15	7													
9	Discharge Planning Conditions	8 wks	Mon 20/07/15	Fri 11/09/15	13													
10	Judicial Review Stand-Off Period	30 days	Mon 20/07/15	Fri 28/08/15	8													
11	Complete detailed CPs	12 wks	Mon 23/03/15	Fri 12/06/15	4													
12	Final Business Case Submission	0 days	Mon 15/06/15	Mon 15/06/15	11													
13	FBC Approval	4 wks	Mon 15/06/15	Fri 10/07/15	11													
14	OMBC demolition and Land Assembly	12 wks	Mon 31/08/15	Fri 20/11/15	10													
15	Contract Award	1 day	Mon 23/11/15	Mon 23/11/15	14													
16	Mobilisation	4 wks	Tue 24/11/15	Mon 21/12/15	15													
17	Construction Period and External Works	17.35 mons	Mon 21/12/15	Tue 18/04/17	16													
18	New Building Complete and Handed Over	0 mons	Tue 18/04/17	Tue 18/04/17	17													
19	School Decant into New Building	2 wks	Tue 04/04/17	Mon 17/04/17														
20	School Open	1 day	Tue 18/04/17	Tue 18/04/17	19													



Project: Grangefield Gantt Chart
Date: Tue 20/01/15


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

December			January				February				March				April				May							
09/12	16/12	23/12	30/12	06/01	13/01	20/01	27/01	03/02	10/02	17/02	24/02	03/03	10/03	17/03	24/03	31/03	07/04	14/04	21/04	28/04	05/05	12/05	19/05	26/05	02/06	




Project: Grangefield Gantt Chart Date: Tue 20/01/15	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

June			July				August				September				October				November							
09/06	16/06	23/06	30/06	07/07	14/07	21/07	28/07	04/08	11/08	18/08	25/08	01/09	08/09	15/09	22/09	29/09	06/10	13/10	20/10	27/10	03/11	10/11	17/11	24/11	01/12	




Project: Grangefield Gantt Chart Date: Tue 20/01/15	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

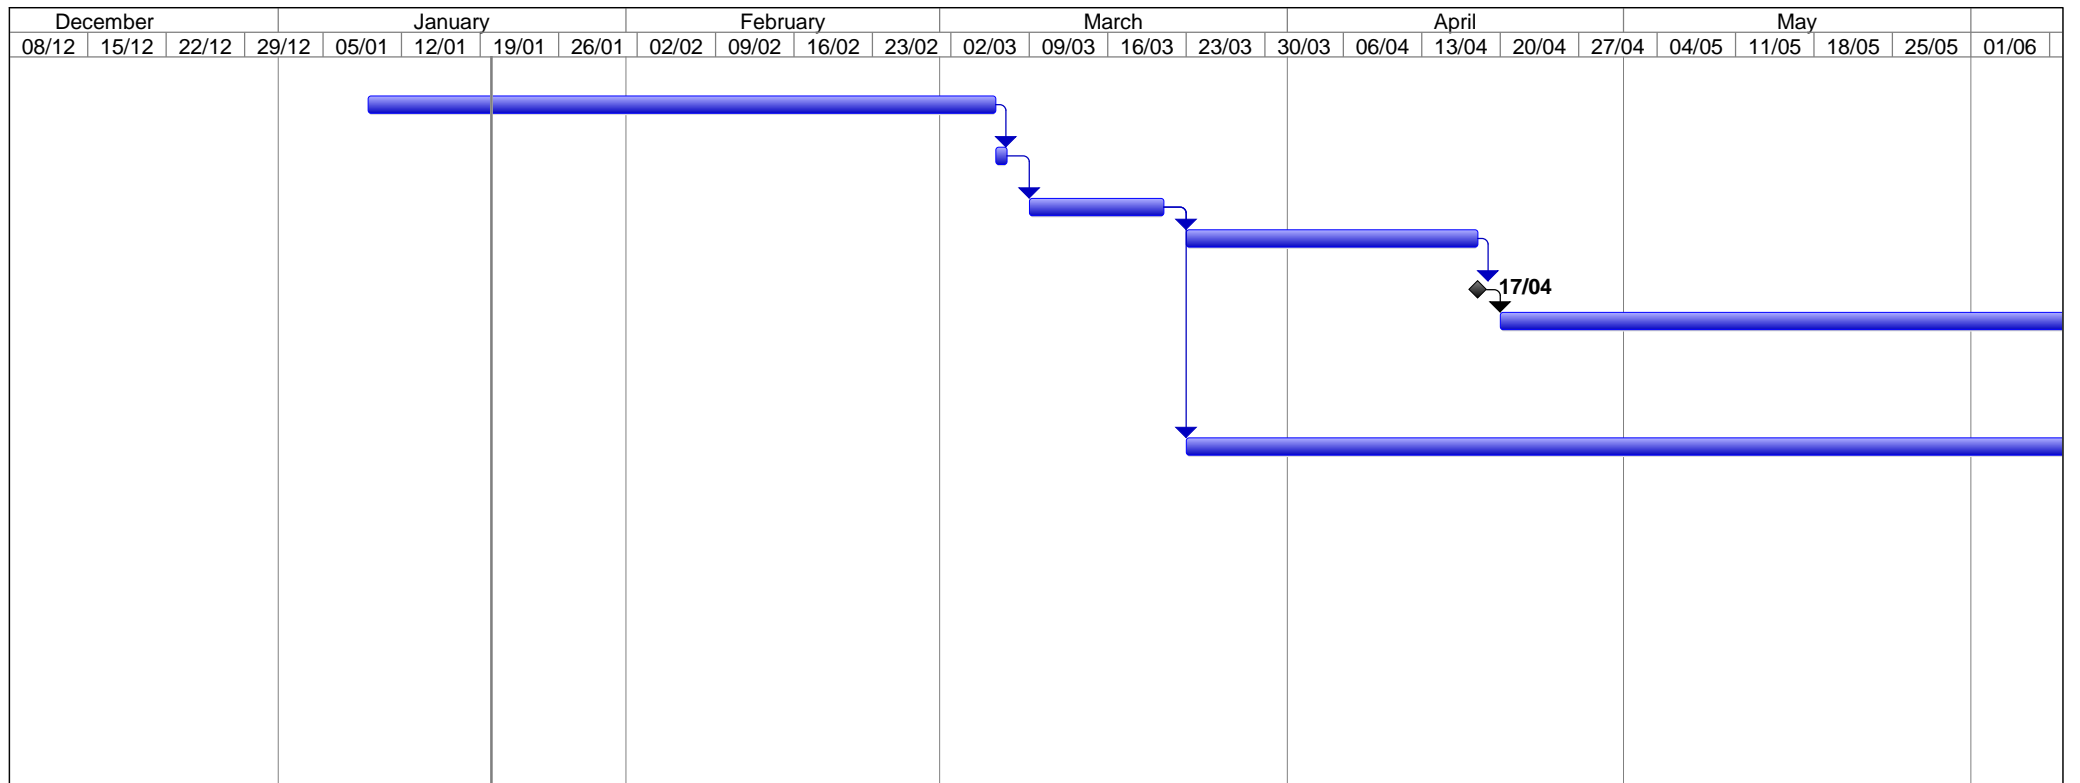


Project: Grangefield Gantt Chart
Date: Tue 20/01/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

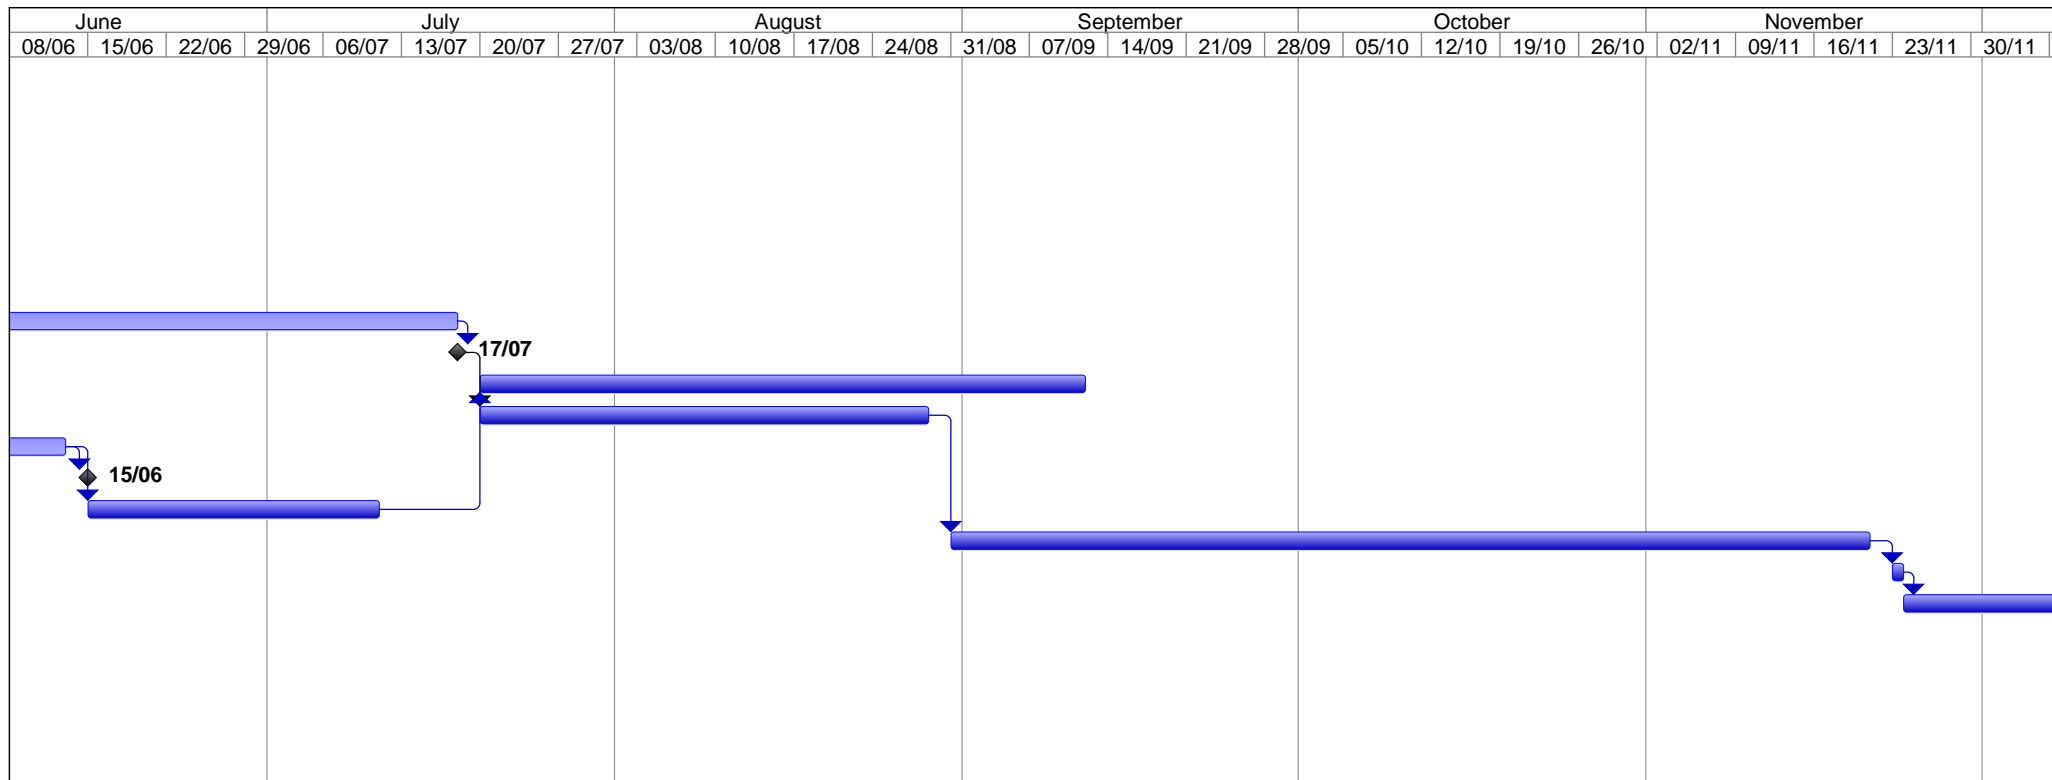

Project: Grangefield Gantt Chart
Date: Tue 20/01/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

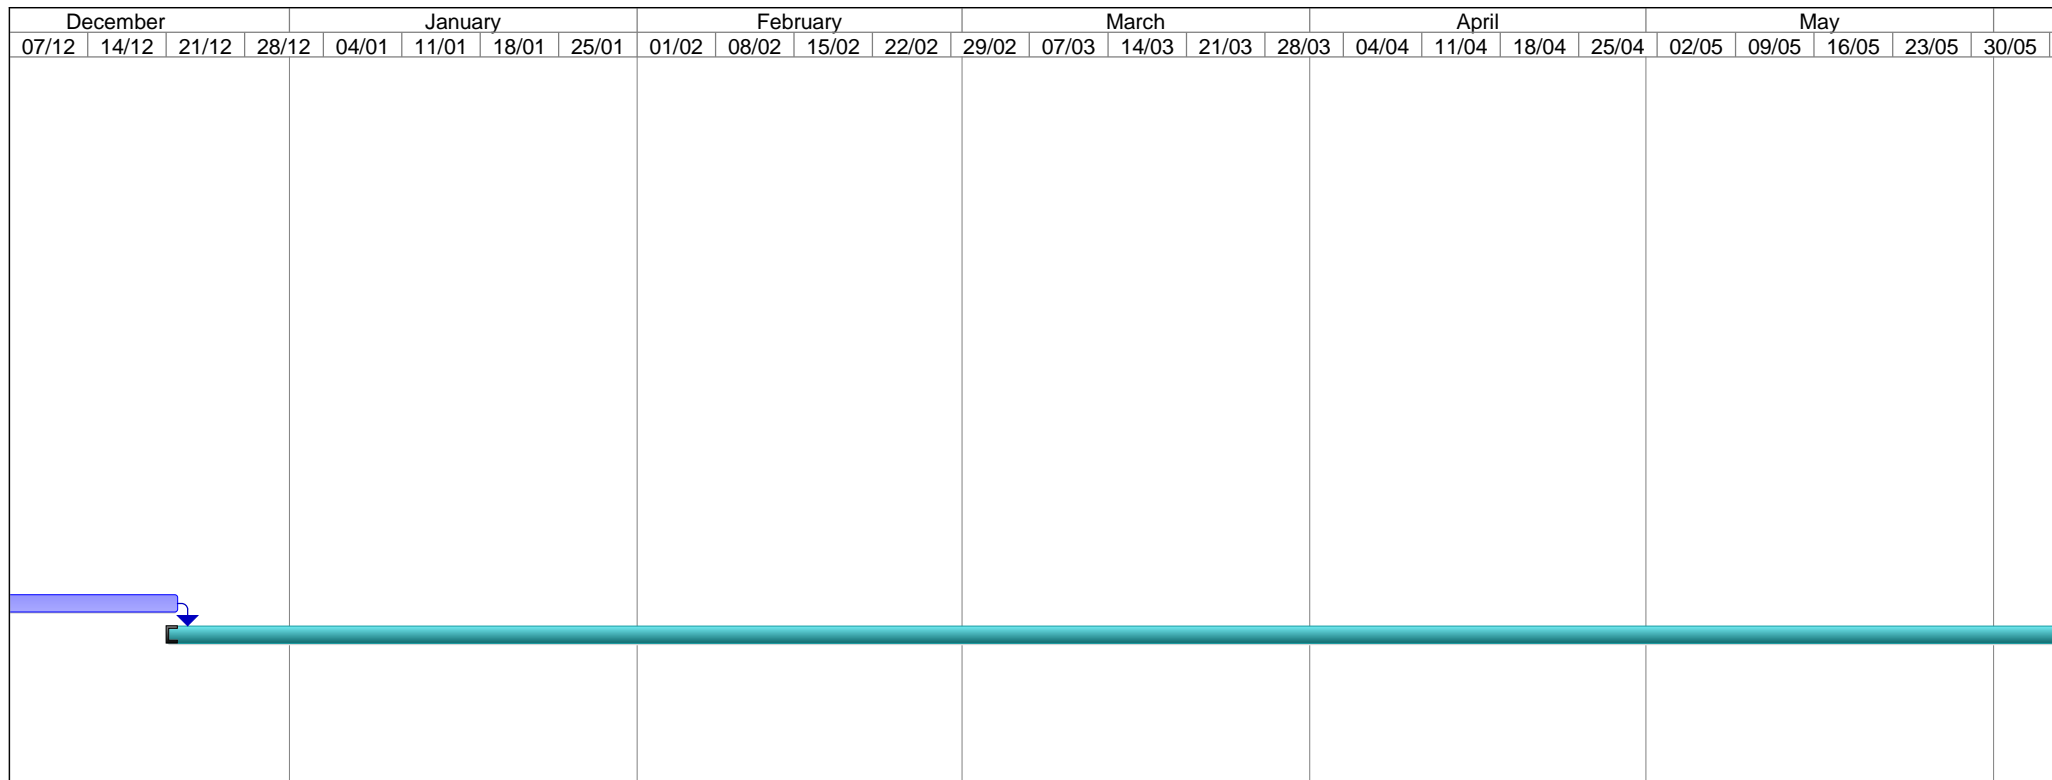




















Project: Grangefield Gantt Chart
Date: Tue 20/01/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

June				July				August				September				October				November							
06/06	13/06	20/06	27/06	04/07	11/07	18/07	25/07	01/08	08/08	15/08	22/08	29/08	05/09	12/09	19/09	26/09	03/10	10/10	17/10	24/10	31/10	07/11	14/11	21/11	28/11		

Project: Grangefield Gantt Chart
Date: Tue 20/01/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

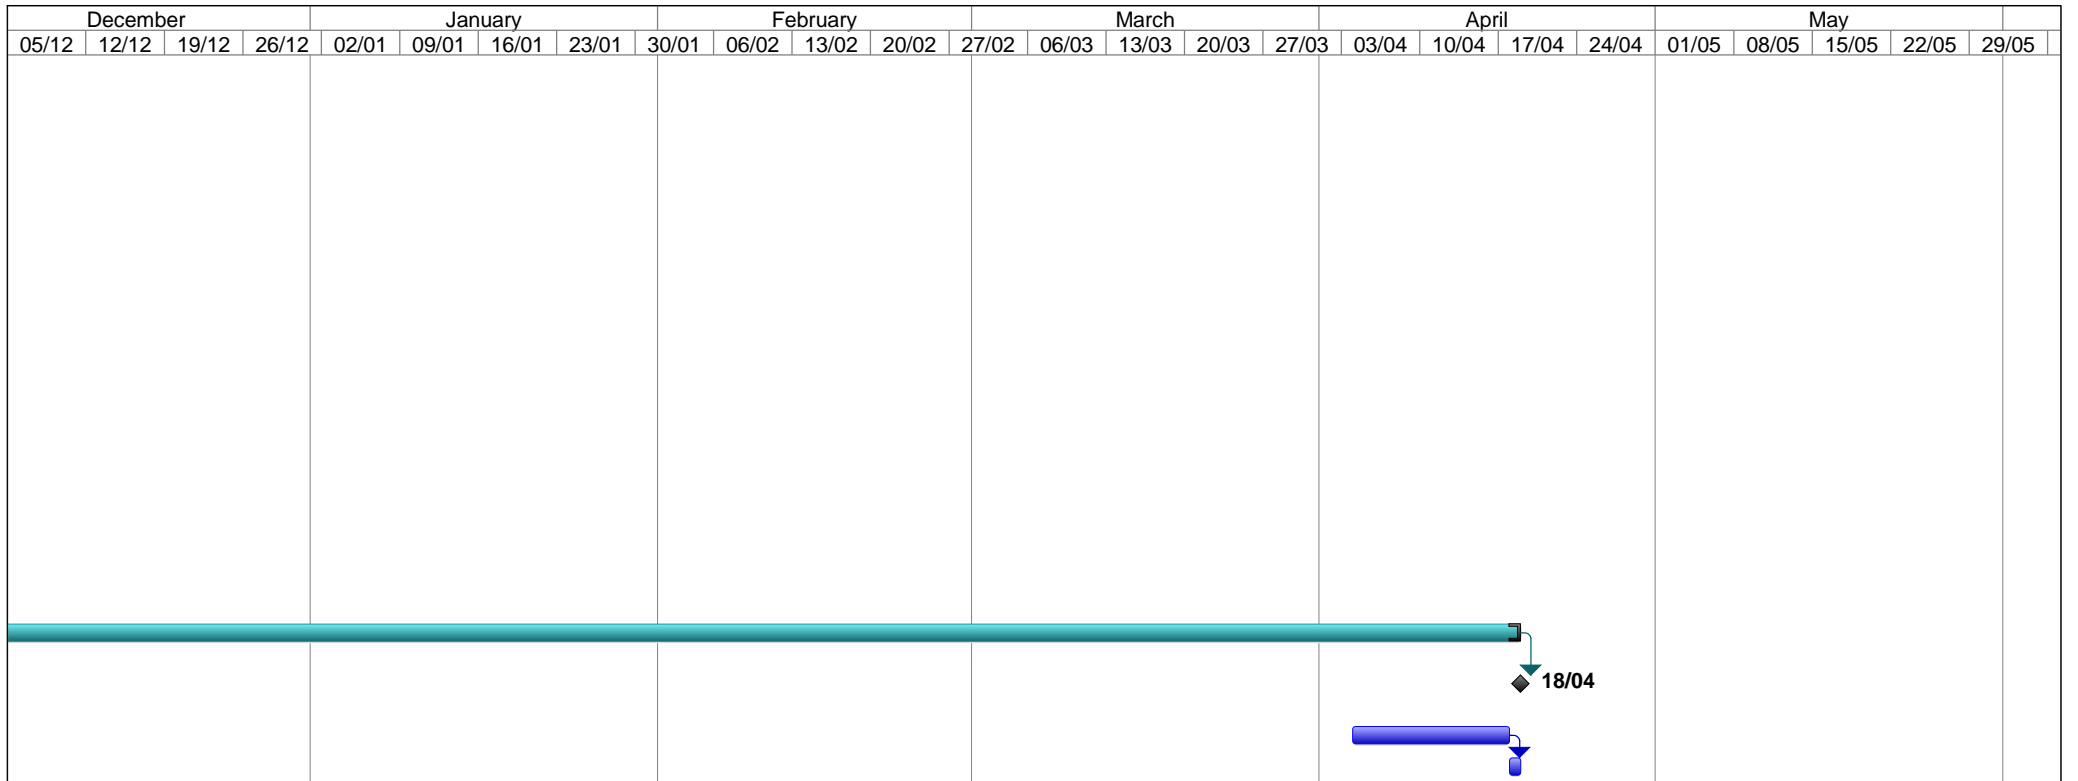

Project: Grangefield Gantt Chart
Date: Tue 20/01/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	
